



ID	Task Mode	Task Name	Working Days	Start	Finish	Predecessors	022													
							Feb	Mar	Qtr 3, 2022			Qtr 4, 2022			Qtr 1, 2023			Qtr 2, 2023		
							Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	
1		City Council Meeting/ Contract Approval	0 days	Tue 3/22/22	Tue 3/22/22															
2		Contract Execution	30 days	Tue 3/22/22	Mon 5/2/22	1														
3		Notice To Proceed	1 day	Tue 5/3/22	Tue 5/3/22	2														
4		Survey	30 days	Wed 5/4/22	Tue 6/14/22	3														
5		Survey (Milestone)	0 days	Tue 6/14/22	Tue 6/14/22	4														
6		Geotechnical Investigation	45 days	Wed 5/4/22	Tue 7/5/22	3														
7		Cultural / Environmental	45 days	Wed 5/4/22	Tue 7/5/22	3														
8		Hydraulic / Hydrologic	45 days	Wed 6/15/22	Tue 8/16/22	4														
9		Design Development	60 days	Wed 6/15/22	Tue 9/6/22	4														
10		Design Development (Milestone)	0 days	Tue 9/6/22	Tue 9/6/22	9														
11		Client Review	10 days	Wed 9/7/22	Tue 9/20/22	10														
12		50% Construction Documents	45 days	Wed 9/21/22	Tue 11/22/22	11														
13		50% CD Submittal (Milestone)	0 days	Tue 11/22/22	Tue 11/22/22	12														
14		Client Review	10 days	Wed 11/23/22	Tue 12/6/22	13														
15		75% Construction Documents	45 days	Wed 12/7/22	Tue 2/7/23	14														
16		75% CD Submittal (Milestone)	0 days	Tue 2/7/23	Tue 2/7/23	15														
17		Client Review	10 days	Wed 2/8/23	Tue 2/21/23	15														
18		95% Construction Documents	25 days	Wed 2/22/23	Tue 3/28/23	17														
19		95% CD Submittal (Milestone)	0 days	Tue 3/28/23	Tue 3/28/23	18														
20		Client Review	10 days	Wed 3/29/23	Tue 4/11/23	19														
21		Bid Issue Construction Documents	15 days	Wed 4/12/23	Tue 5/2/23	20														
22		Bid Issue CD Submittal (Milestone)	0 days	Tue 5/2/23	Tue 5/2/23	21														
23		Bidding Phase	30 days	Wed 5/3/23	Tue 6/13/23	22														
24		Bid Date	0 days	Tue 6/13/23	Tue 6/13/23	23														
25		Contract Award Date/NTP	30 days	Wed 6/14/23	Tue 7/25/23	24														
26		Construction Kickoff Meeting	5 days	Wed 7/26/23	Tue 8/1/23	25														
27		Construction Admin Phase	330 days	Wed 8/2/23	Tue 11/5/24	26														
28		CA Onsite Meetings	341 days	Tue 8/8/23	Tue 11/26/24	26														
64		Substantial Completion	20 days	Wed 11/6/24	Tue 12/3/24	27														
65		Project Closeout	30 days	Wed 12/4/24	Tue 1/14/25	64														
66		Final Completion/Payapp	0 days	Tue 1/14/25	Tue 1/14/25	65														
67		12 Month Warranty Walkthrough	0 days	Tue 1/13/26	Tue 1/13/26															

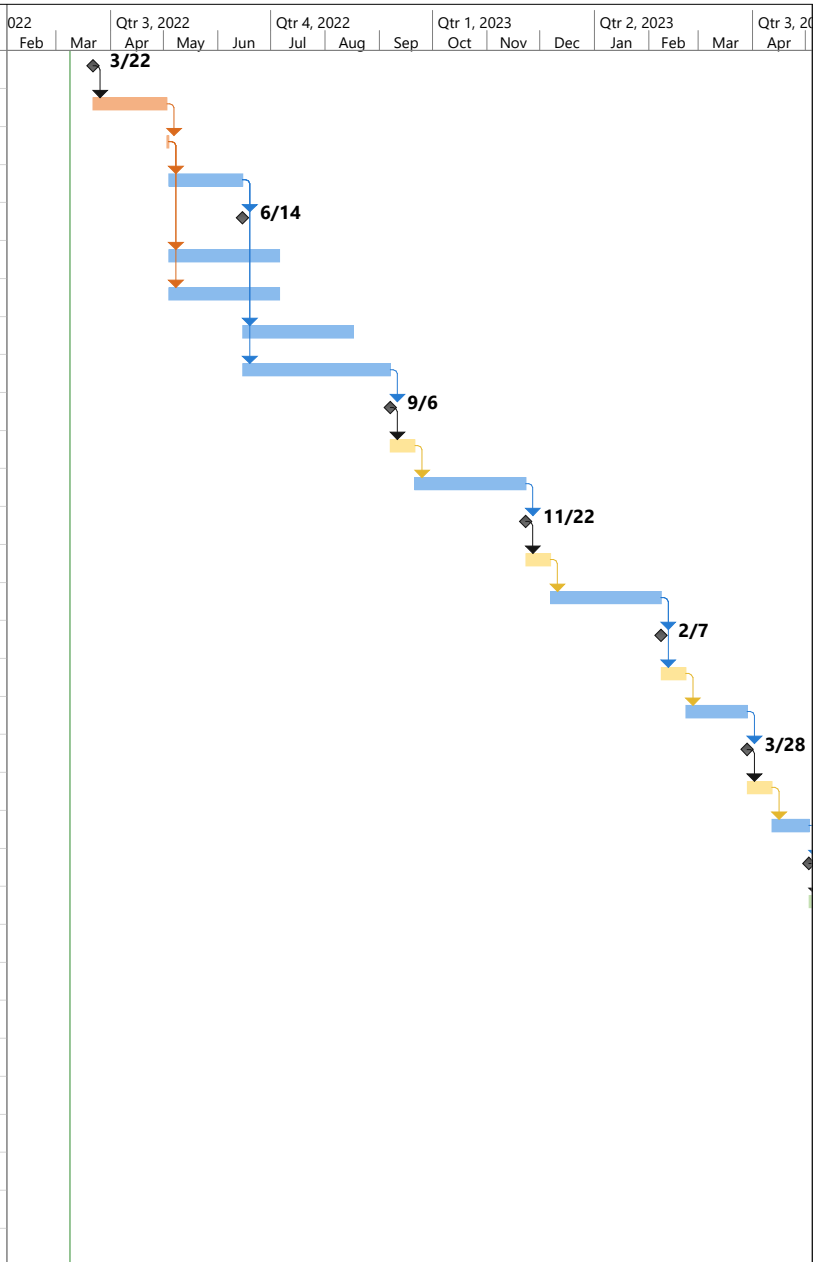

Project: Keller Sports Park - Sch
Date: Wed 3/9/22

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

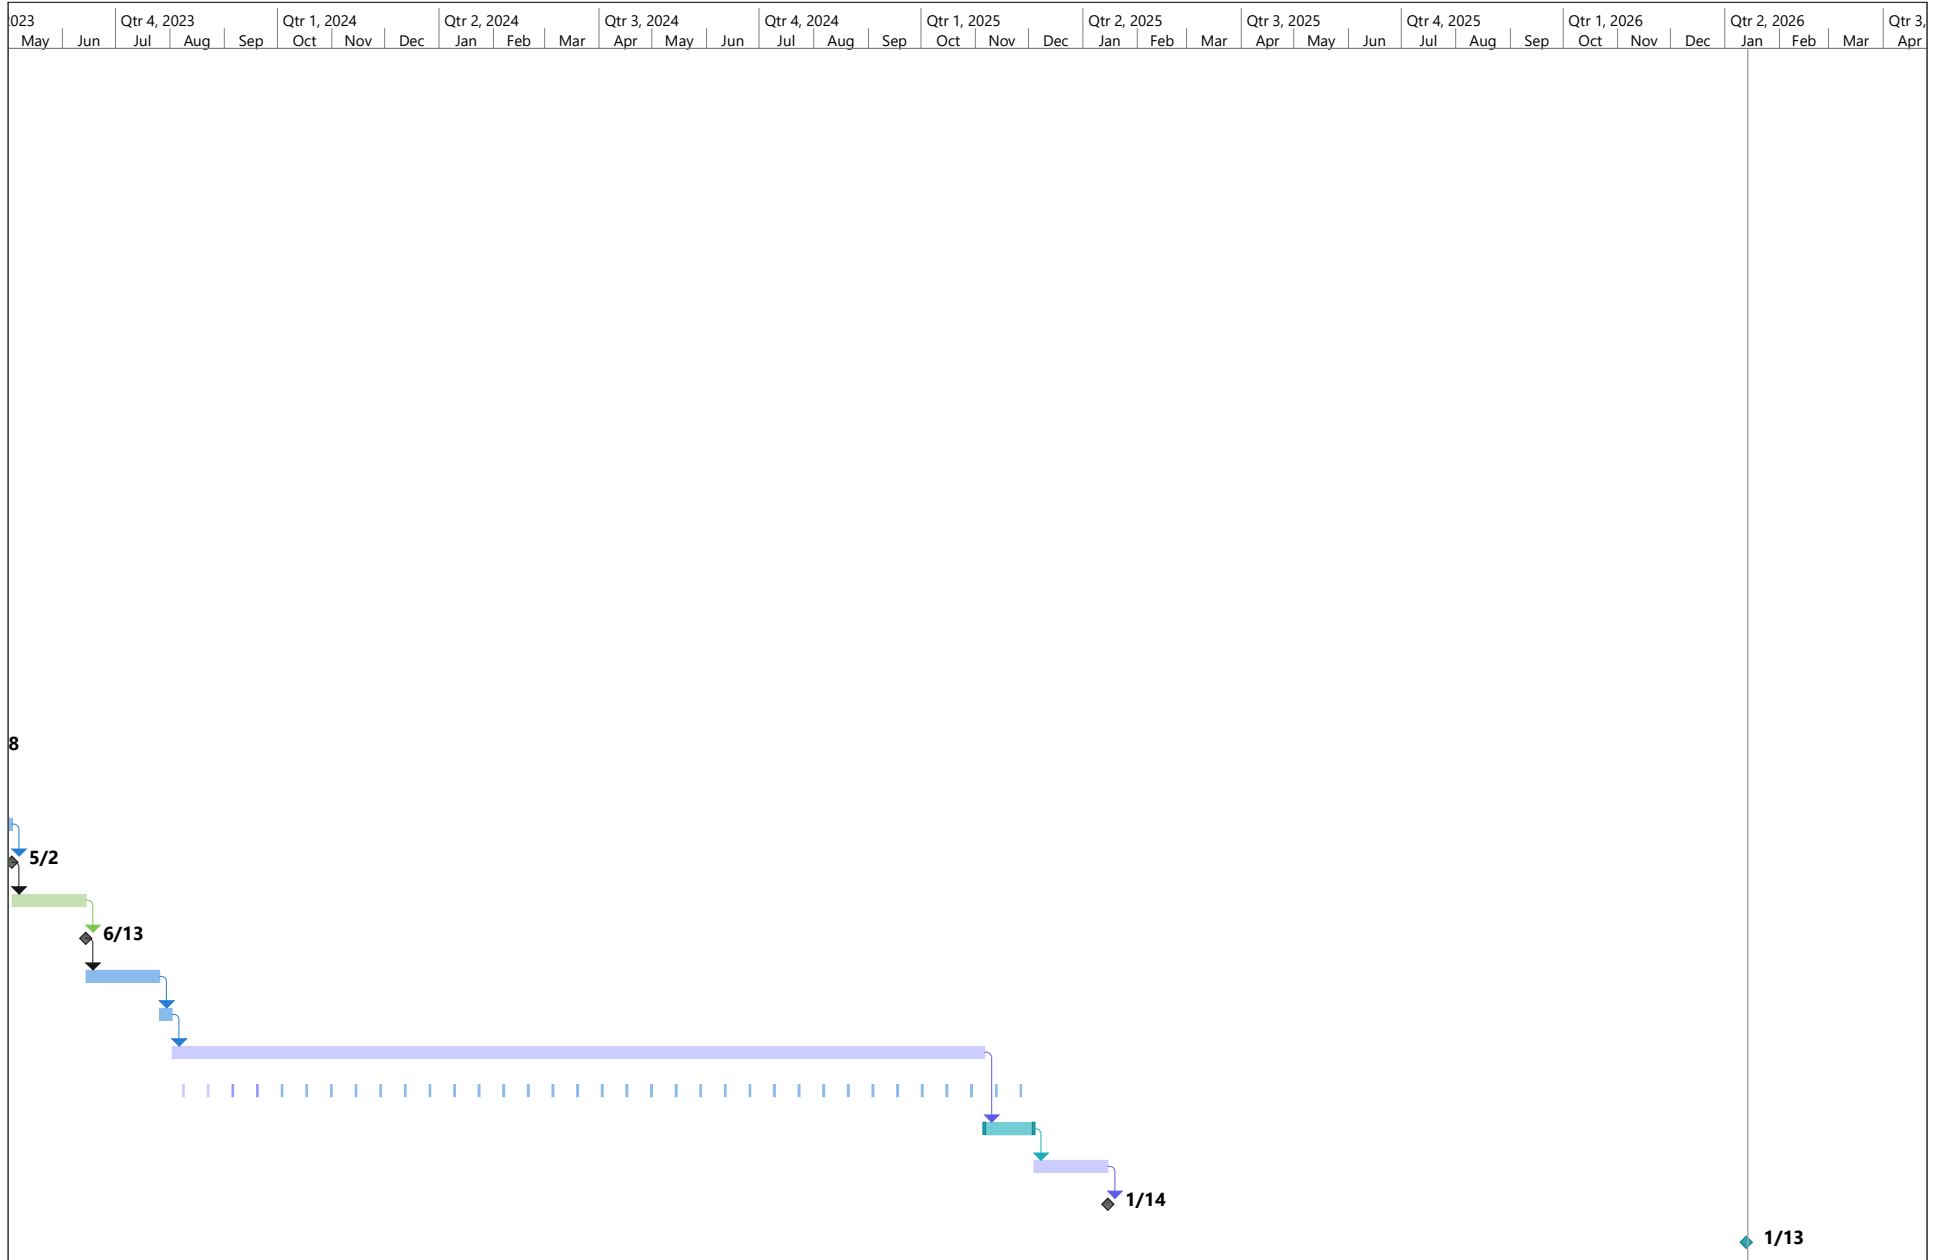

Project: Keller Sports Park - Sch Date: Wed 3/9/22	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			
